

Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

Activity ID	Activity Name	Duration	Remaining Duration	Start	Finish	Total Float	Duration % Complete	2026					
								Feb 48	Mar 49	Apr 50	May 51	Jun 52	Jul 53
Construction of Siu Ho Wan Water Treatment Works		1781d	439d	27-Jun-22 A	12-May-27	-56d	75.35%						
Section of the Works (Revised Completion Date)		29d	29d	17-Mar-26	15-Apr-26	0d	0%	Section of the Works (Revised Completion Date)					
SEW1160	Section 2- Installation and modification works for Water Treatment Build	0d	0d		17-Mar-26*	0d	0%	Section 2- Installation and modification works for Water Treatment Building,Office and Laboratory,Chemical building,etc					
SEW1170	Section 3- E&M installation works for Siu Ho Wan Raw Water Booster P	0d	0d		17-Mar-26*	0d	0%	Section 3- E&M installation works for Siu Ho Wan Raw Water Booster Pumping Station, road works and remaining works					
SEW1190	Section 4- Landscape softworks and establishment works	0d	0d		15-Apr-26*	0d	0%	Section 4- Landscape softworks and establishment works					
Section of the Works (Planned Completion Date)		4d	4d	08-May-26	12-May-26	-56d	0%	Section of the Works (Planned Completion Date)					
SEW1050	Section 2- Installation and modification works for Water Treatment Build	0d	0d		12-May-26	-56d	0%	Section 2- Installation and modification works for Water Tre					
SEW1060	Section 3- E&M installation works for Siu Ho Wan Raw Water Booster P	0d	0d		08-May-26	-52d	0%	Section 3- E&M installation works for Siu Ho Wan Raw Water B					
Defect Date for Each Section of the Works		834d	439d	29-Jan-25 A	12-May-27	-56d	47.36%						
SEW1100	Section 1- Construction of Water Treatment Building, Siu Ho Wan Raw V	365d	243d	01-Sep-25 A	28-Oct-26*	-49d	33.42%						
SEW1110	Section 2- Installation and modification works for Water Treatment Build	365d	365d	13-May-26	12-May-27*	-56d	0%						
SEW1120	Section 3- E&M installation works for Siu Ho Wan Raw Water Booster P	365d	365d	09-May-26	08-May-27*	-52d	0%						
SEW1140	Section 3A-Entrustment Works	365d	29d	29-Jan-25 A	28-Mar-26*	-59d	92.05%						
Section 2 of the Works		1494d	74d	27-Jun-22 A	12-May-26	-52d	95.05%	Section 2 of the Works					
Water Treatment Building		1432d	74d	27-Jun-22 A	12-May-26	-52d	94.83%	Water Treatment Building					
Architectural Works		272d	57d	28-Jun-25 A	25-Apr-26	-56d	79.04%	Architectural Works					
S110760.2	Finishing works from +25.0mPD up to +29.5mPD floor for DAF Mainte	30d	0d	28-Jun-25 A	04-Mar-26 A		100%						
S110800	Finishing works from +29.5mPD up to +37mPD floor including water ti	25d	0d	05-Nov-25 A	04-Mar-26 A		100%						
S110820	Finishing works from +32.5mPD to +44mPD floor including water tightn	25d	5d	12-Nov-25 A	04-Mar-26	-28d	80%						
S110840	Finishing works from+32.5mPD to +39.0mPD and water tightness test fo	25d	10d	04-Feb-26 A	09-Mar-26	-12d	60%						
S110880.1	Finishing works from+44.0mPD to +50.5mPD floor including PSA, Ozon	25d	10d	28-Nov-25 A	09-Mar-26	-26d	60%						
S110881	Finishing works at roof floor +50.5mPD	60d	15d	09-Nov-25 A	14-Mar-26	-29d	75%						
S110882	Finishing works of external wall	15d	15d	12-Mar-26	26-Mar-26	-27d	0%						
S223170	Construction of planter on the roof	45d	45d	28-Feb-26	25-Apr-26	-44d	0%						
S223200	Installation of external facade	30d	30d	28-Feb-26	08-Apr-26	-29d	0%						
S223205	Installation of vertical greening system	30d	30d	28-Feb-26	08-Apr-26	-29d	0%						
Statutory Submission schedule		1432d	71d	27-Jun-22 A	09-May-26	-53d	95.04%	Statutory Submission schedule					
GBP Submission and Approval		180d	20d	30-Nov-25 A	19-Mar-26	-52d	88.89%	GBP Submission and Approval					
S211991	Submission/Review/Approval by PM and FSD - 4th submission (To suit i	180d	10d	30-Nov-25 A	09-Mar-26	-52d	94.44%						
S212001	4th GBP Approval from FSD	10d	10d	10-Mar-26	19-Mar-26	-52d	0%						
DG Application and Approval		1413d	71d	27-Jun-22 A	09-May-26	-53d	94.98%	DG Application and Approval					
S210060	DG (Ozone) installation approval - dwg & layout by FSD for WTB	680d	10d	27-Jun-22 A	09-Mar-26	-52d	98.53%						
S210065	Design works and re-submission to address FSD's Comment	100d	5d	10-Jul-24 A	04-Mar-26	-47d	95%						
S210080	DG application letter - DG store (Oxygen tank) for WTB	16d	16d	10-Mar-26	27-Mar-26	-41d	0%						
S210100	DG acknowledgement and "No objection" letter from FSD	10d	10d	28-Mar-26	13-Apr-26	-41d	0%						
S210140	Vent/425 DG completion inspection for WTB	5d	5d	23-Apr-26	27-Apr-26	-53d	0%						
S210160	DG (Ozone & oxygen tank) - inform FSD for installation completion insp	15d	15d	18-Mar-26	01-Apr-26	-27d	0%						
S210180	FS_Certificate (Acceptance memo) for WTB	10d	10d	28-Apr-26	07-May-26	-53d	0%						
S210200	FSD issue DG certificate for WTB	10d	10d	28-Apr-26	09-May-26	-41d	0%						
FSI/314 for FS Installation Submission		7d	7d	29-Mar-26	04-Apr-26	-18d	0%	FSI/314 for FS Installation Submission					
S210120	FS_Form FSI314,FSI501 & As-built dwgs for WTB	7d	7d	29-Mar-26	04-Apr-26	-18d	0%						
WSD-Submit Form WWO 542 for Water Supply Application		12d	12d	28-Feb-26	11-Mar-26	-34d	0%	WSD-Submit Form WWO 542 for Water Supply Application					
S210235	WW046 submission to WSD	12d	12d	28-Feb-26	11-Mar-26	-34d	0%						
WSD-Submit Form WWO 542 for FS Water Supply Application		52d	52d	28-Feb-26	20-Apr-26	-34d	0%	WSD-Submit Form WWO 542 for FS Water Supply Application					
S210250	WW046 submission to WSD	12d	12d	28-Feb-26	11-Mar-26	-34d	0%						
S210255	WSD - Received WWO 46 Part V for water certificate issued by WSD	40d	40d	12-Mar-26	20-Apr-26	-34d	0%						




Date	Revision	Checked	Approved
28-Feb-26	1	CLX	RM

3 Month Rolling Programme -
Mar 2026 to May 2026

(sheet 1 of 10)

Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

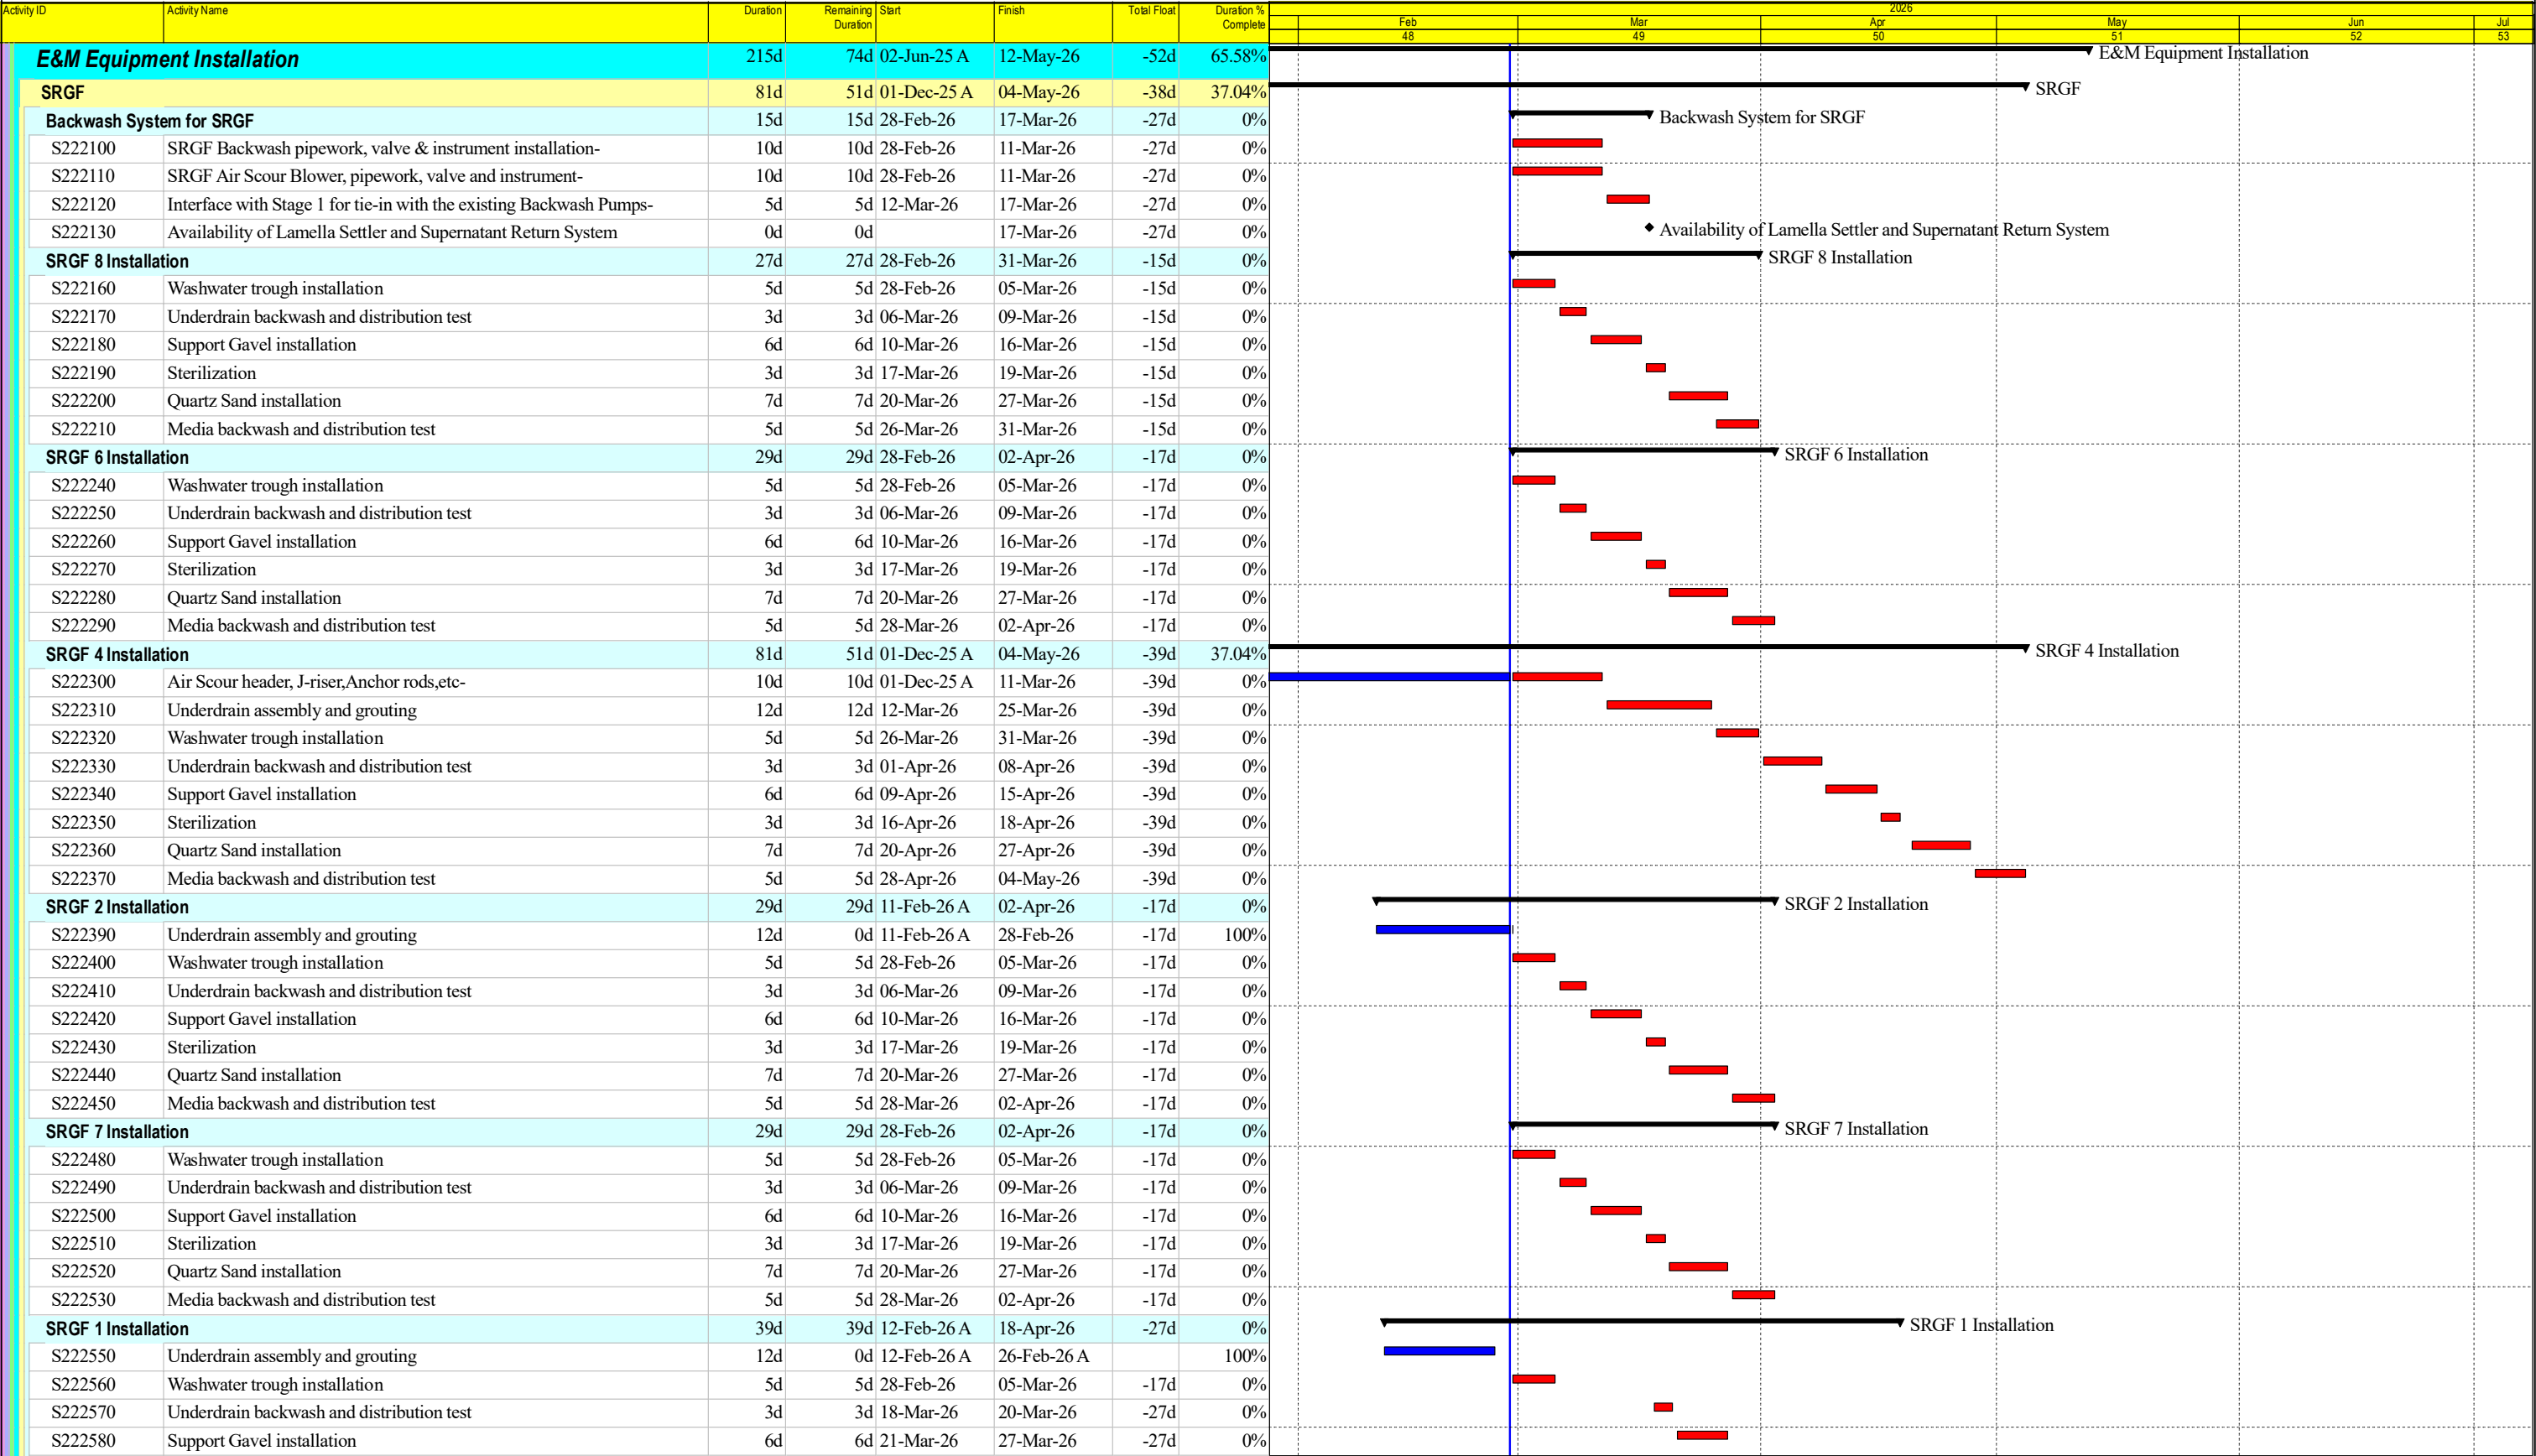

中國路橋
CRBC

- Actual Work
- Non-Critical Activity
- Critical Activity
- ◆

◆ Milestone

Summary


Date	Revision	Checked	Approved
28-Feb-26	1	CLX	RM

3 Month Rolling Programme -
Mar 2026 to May 2026

(sheet 2 of 10)

Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

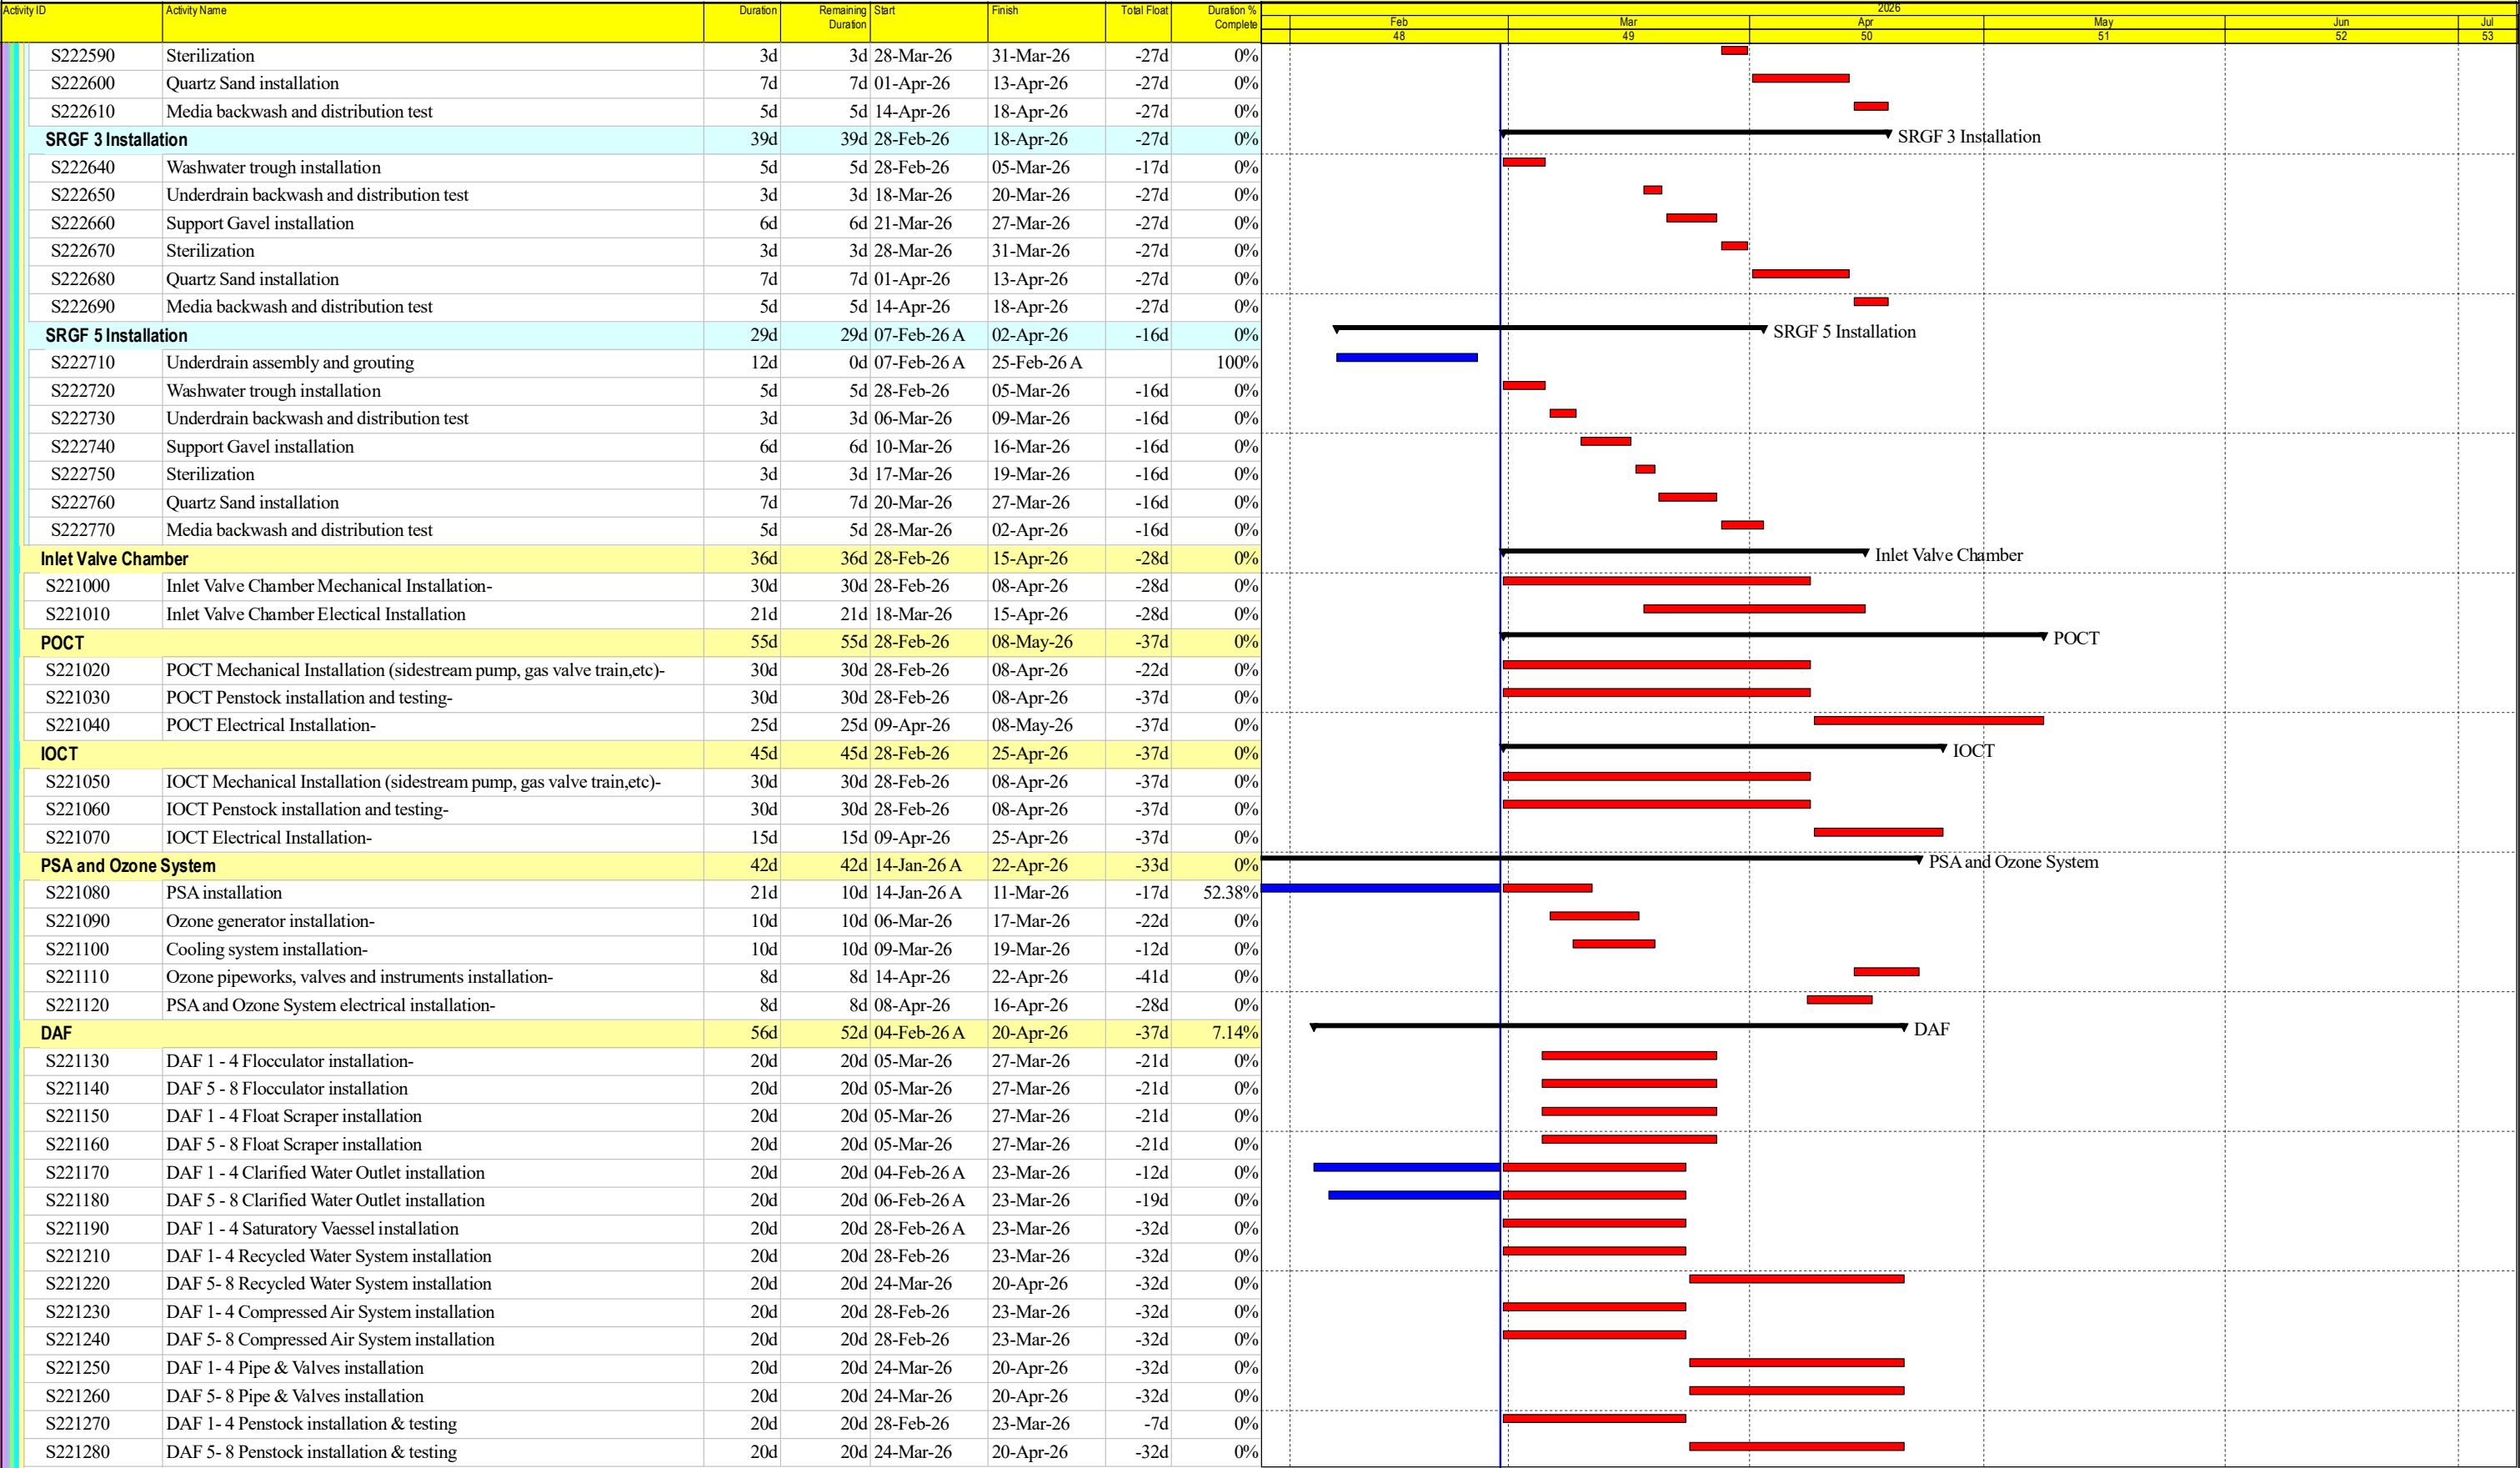

- Actual Work
- Non-Critical Activity
- Critical Activity
- Milestone


Summary

Date	Revision	Checked	Approved
28-Feb-26	1	CLX	RM

3 Month Rolling Programme -
Mar 2026 to May 2026



Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

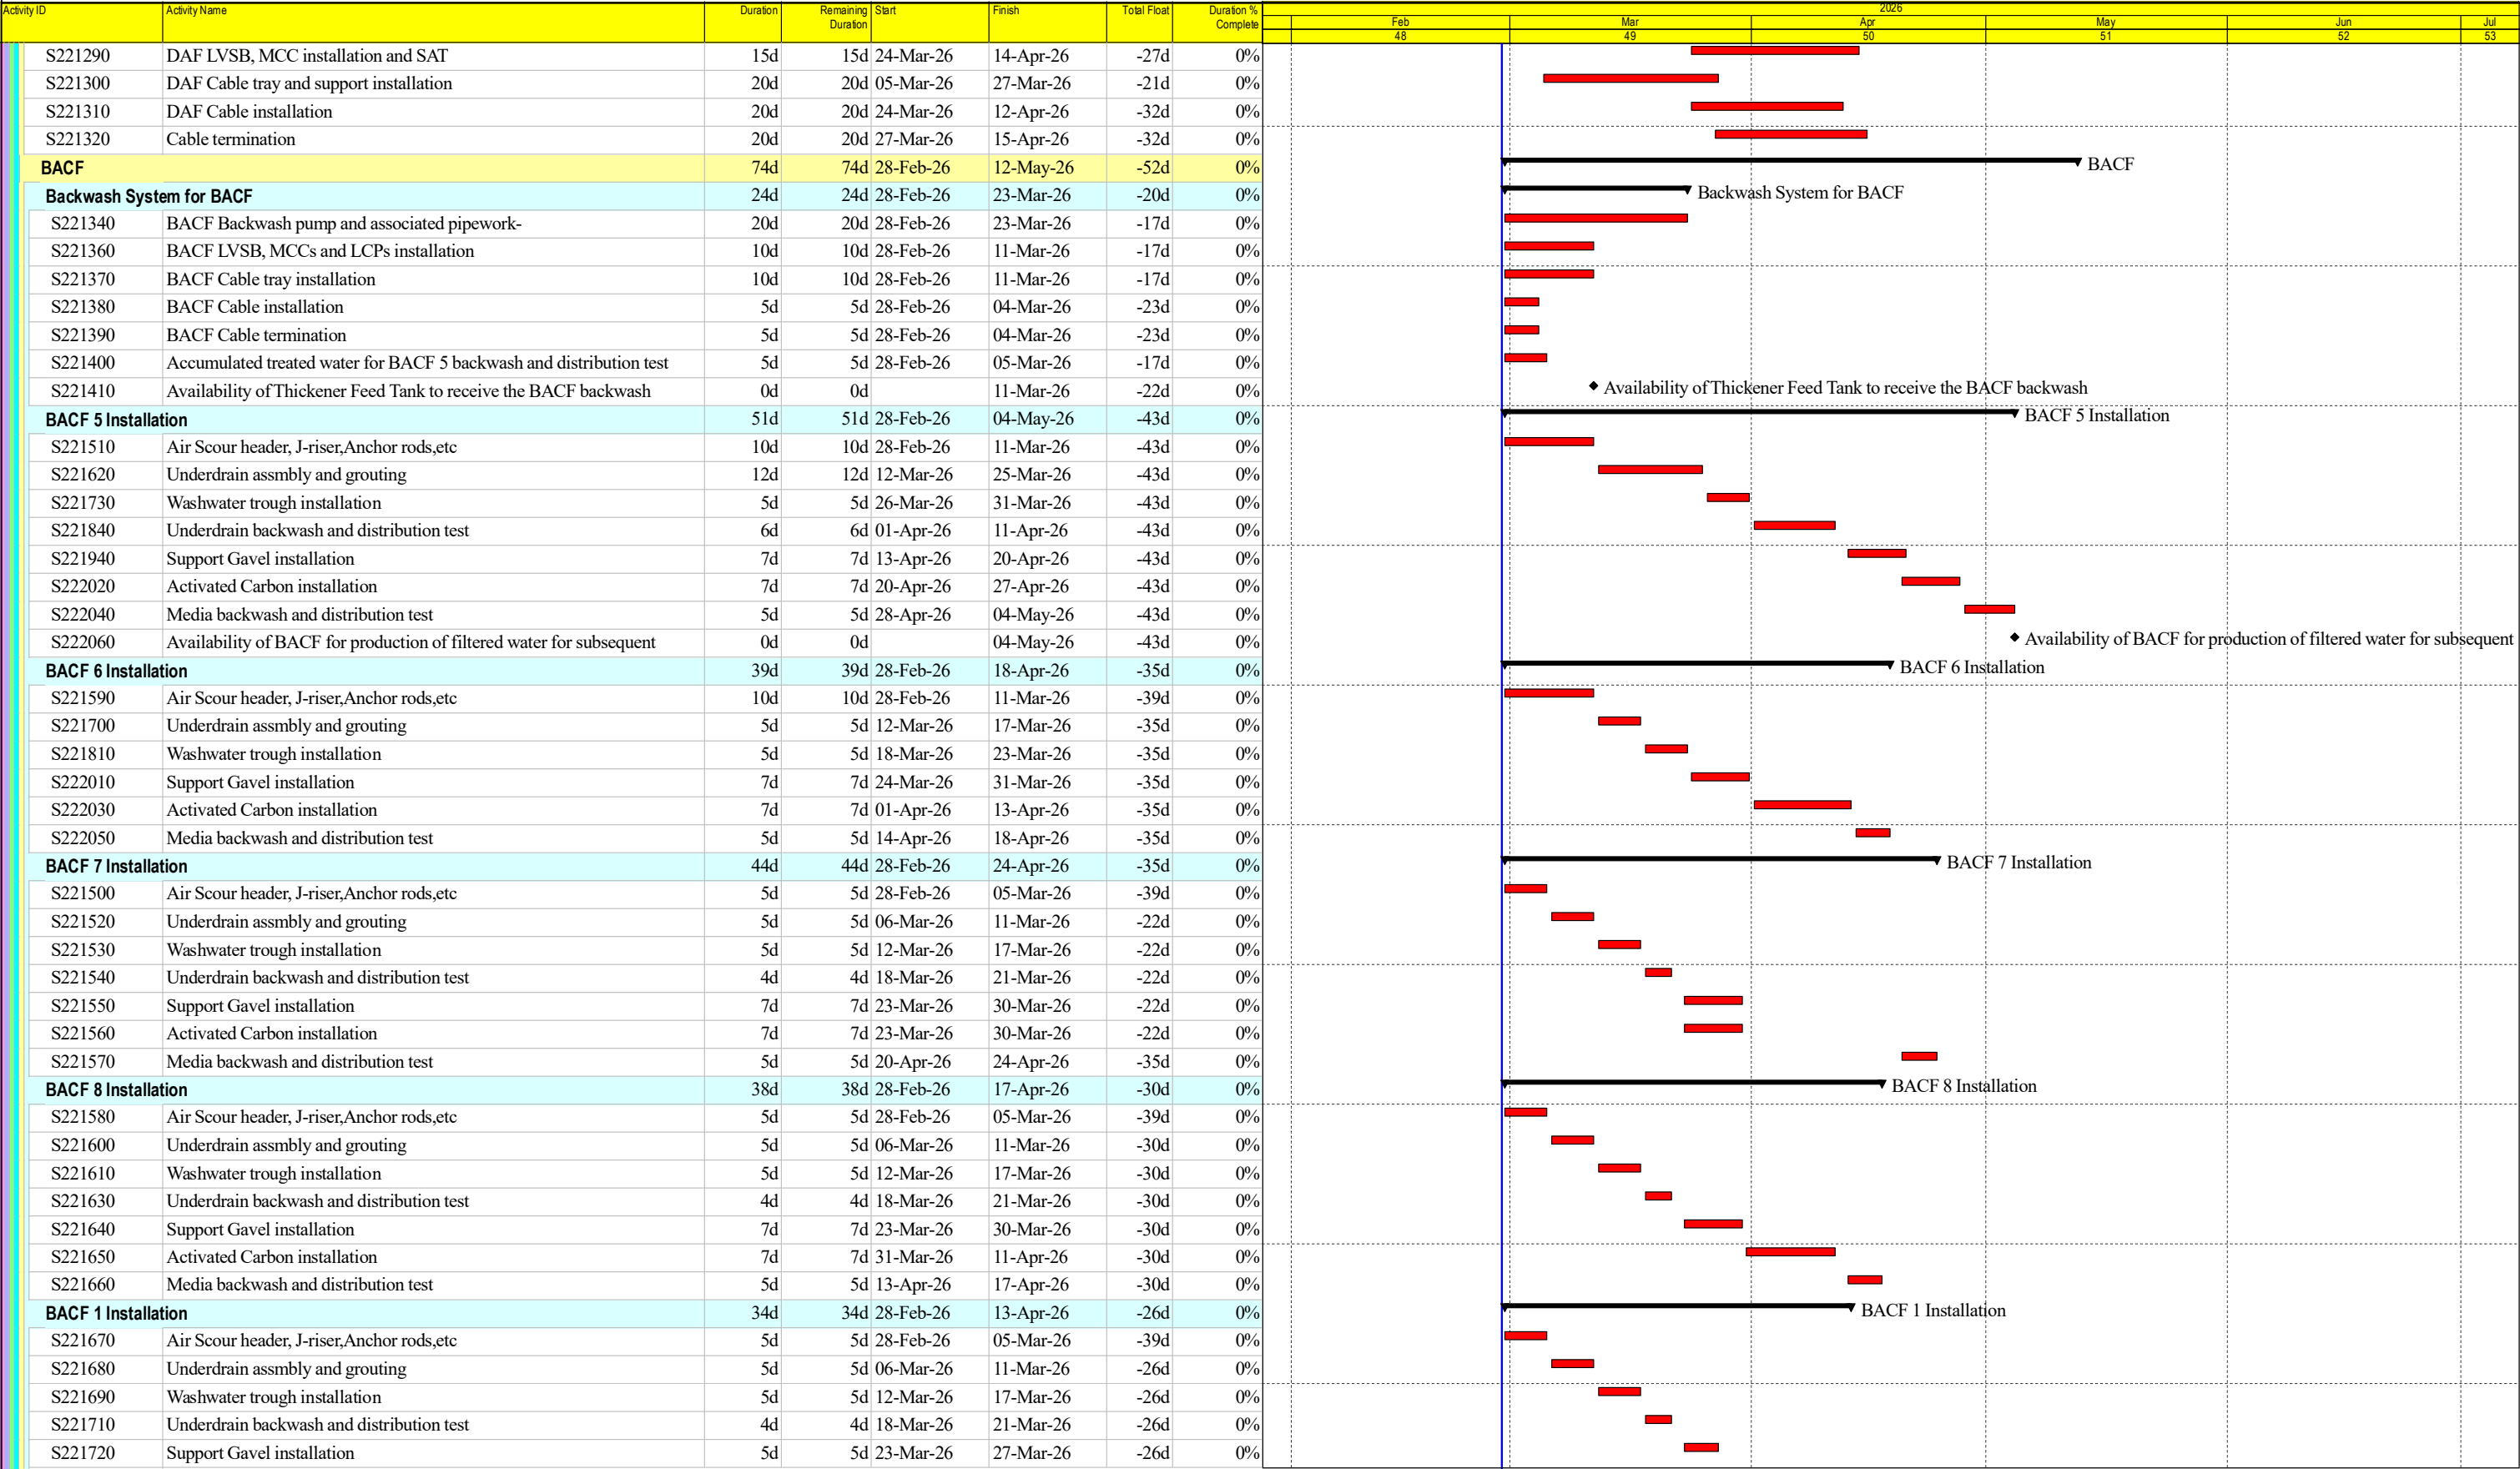

Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

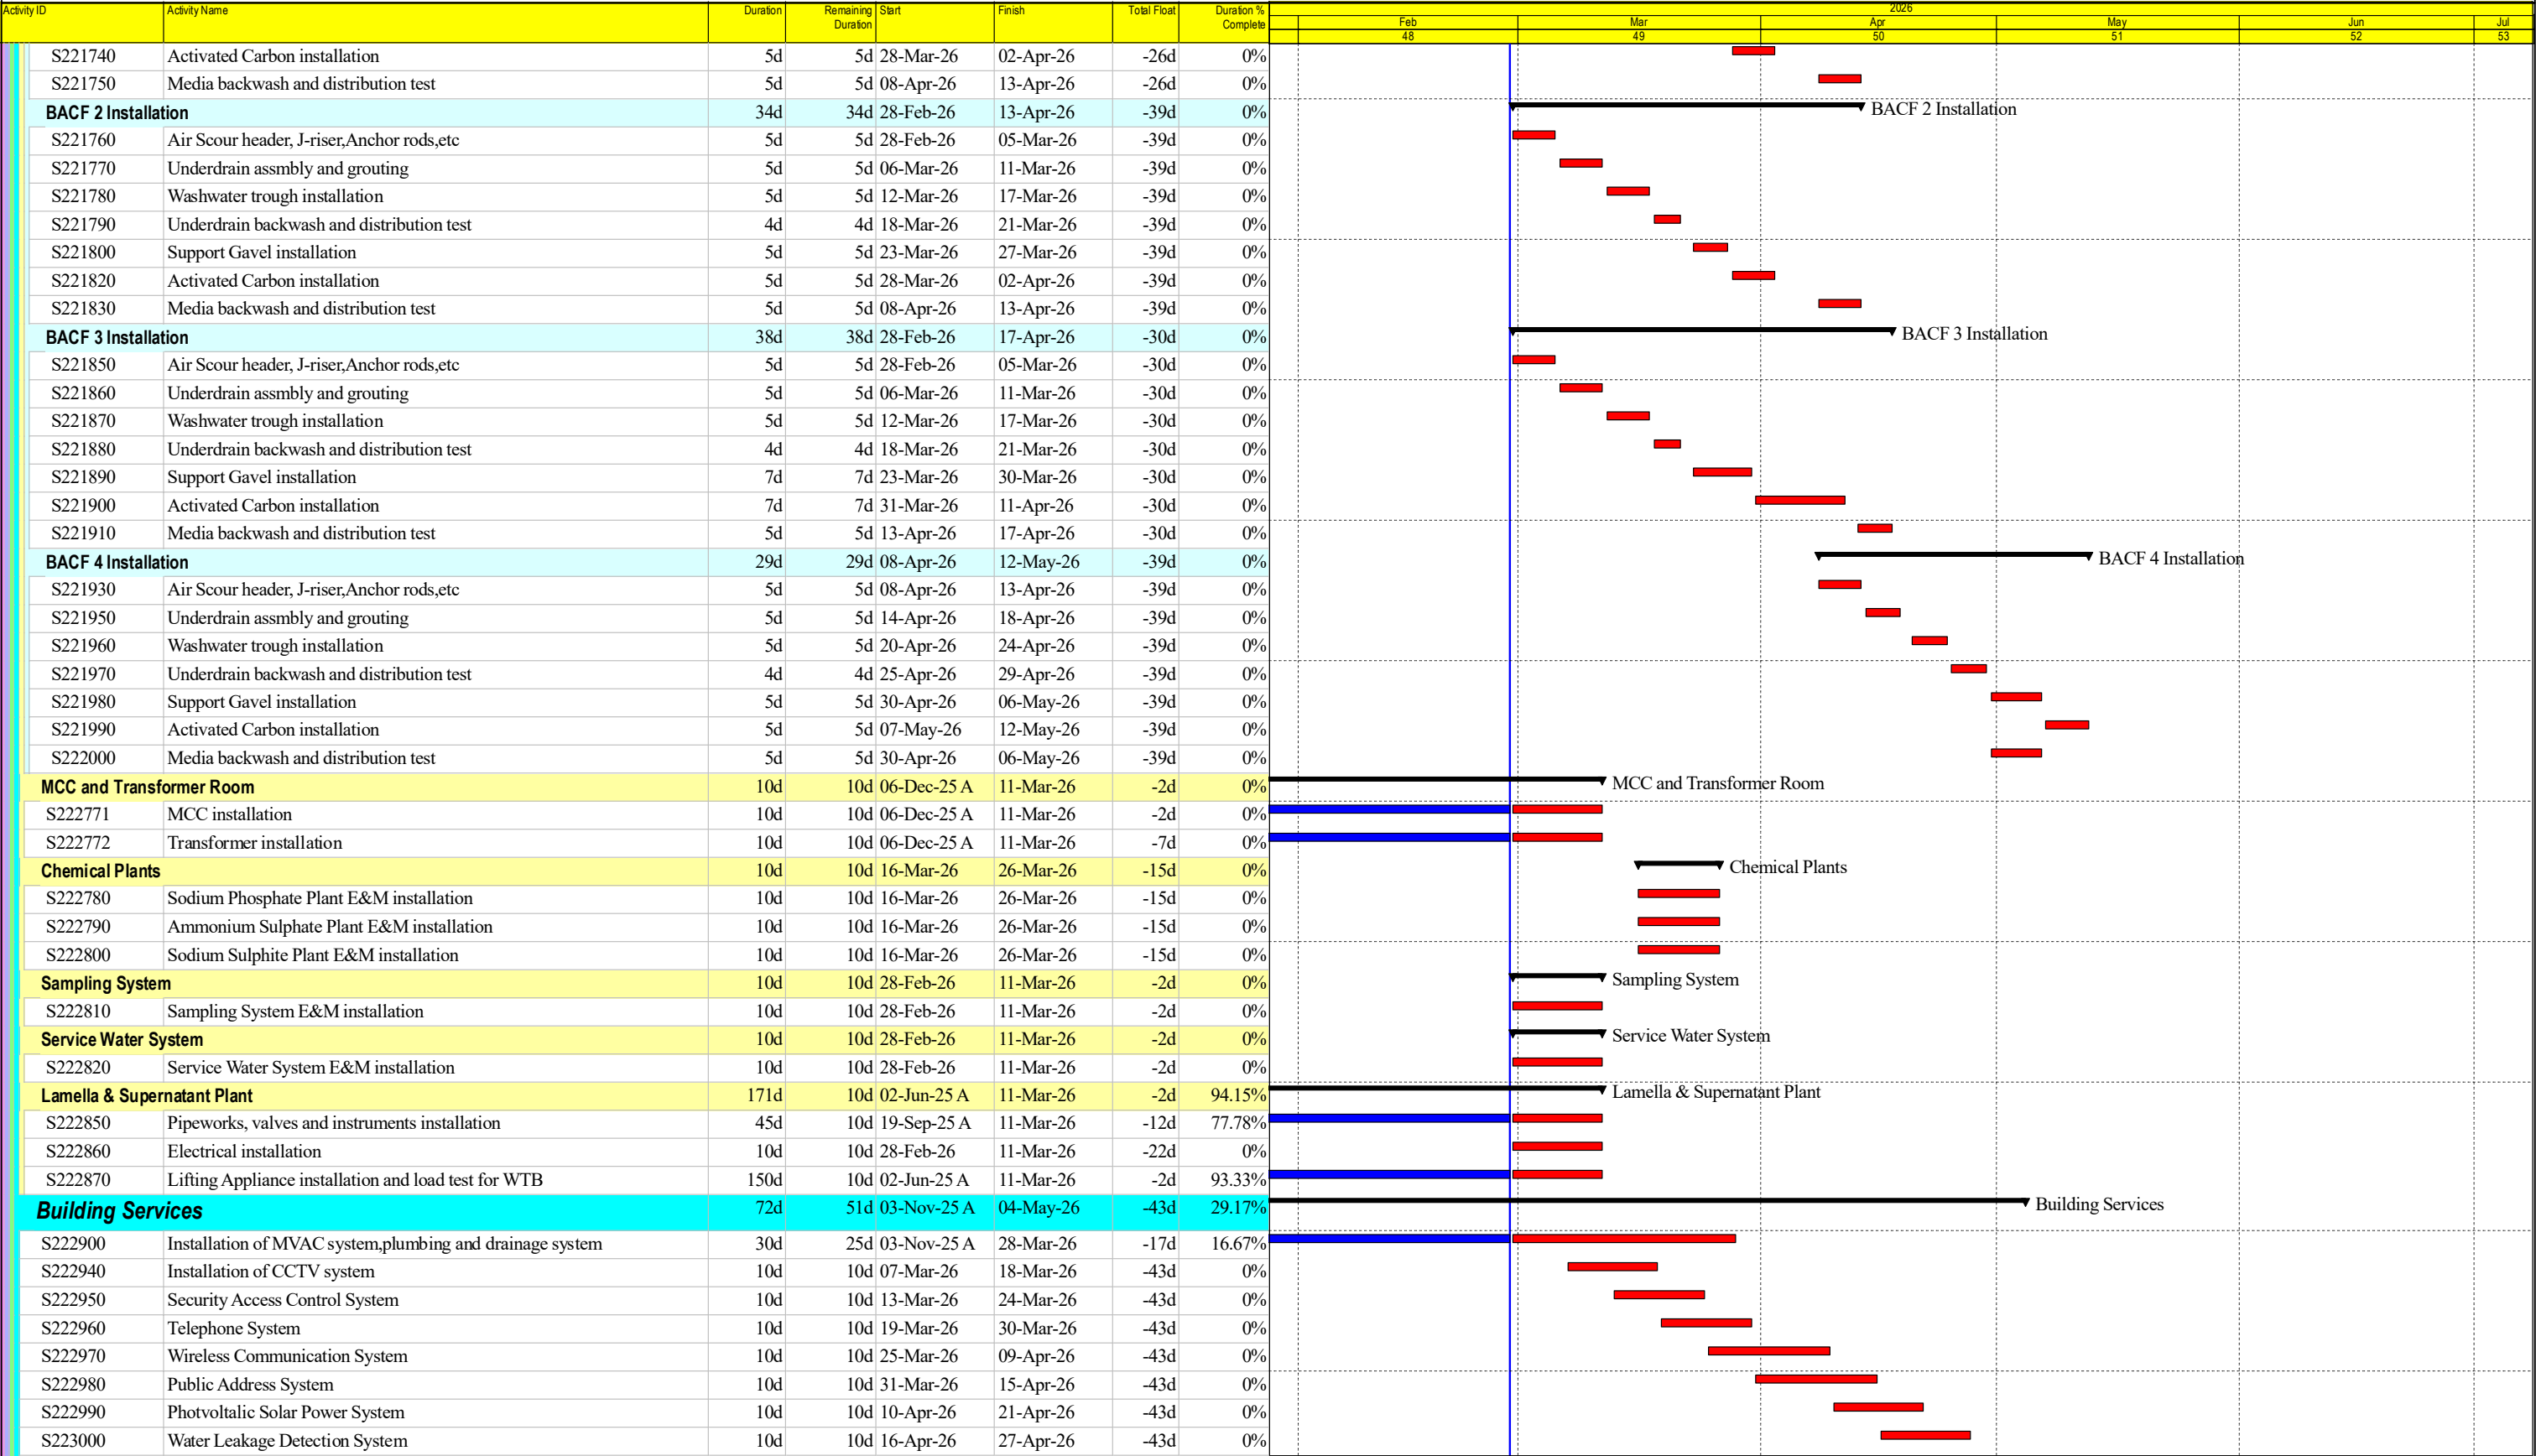


Date	Revision	Checked	Approved
28-Feb-26	1	CLX	RM

3 Month Rolling Programme -
Mar 2026 to May 2026

(sheet 5 of 10)


Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

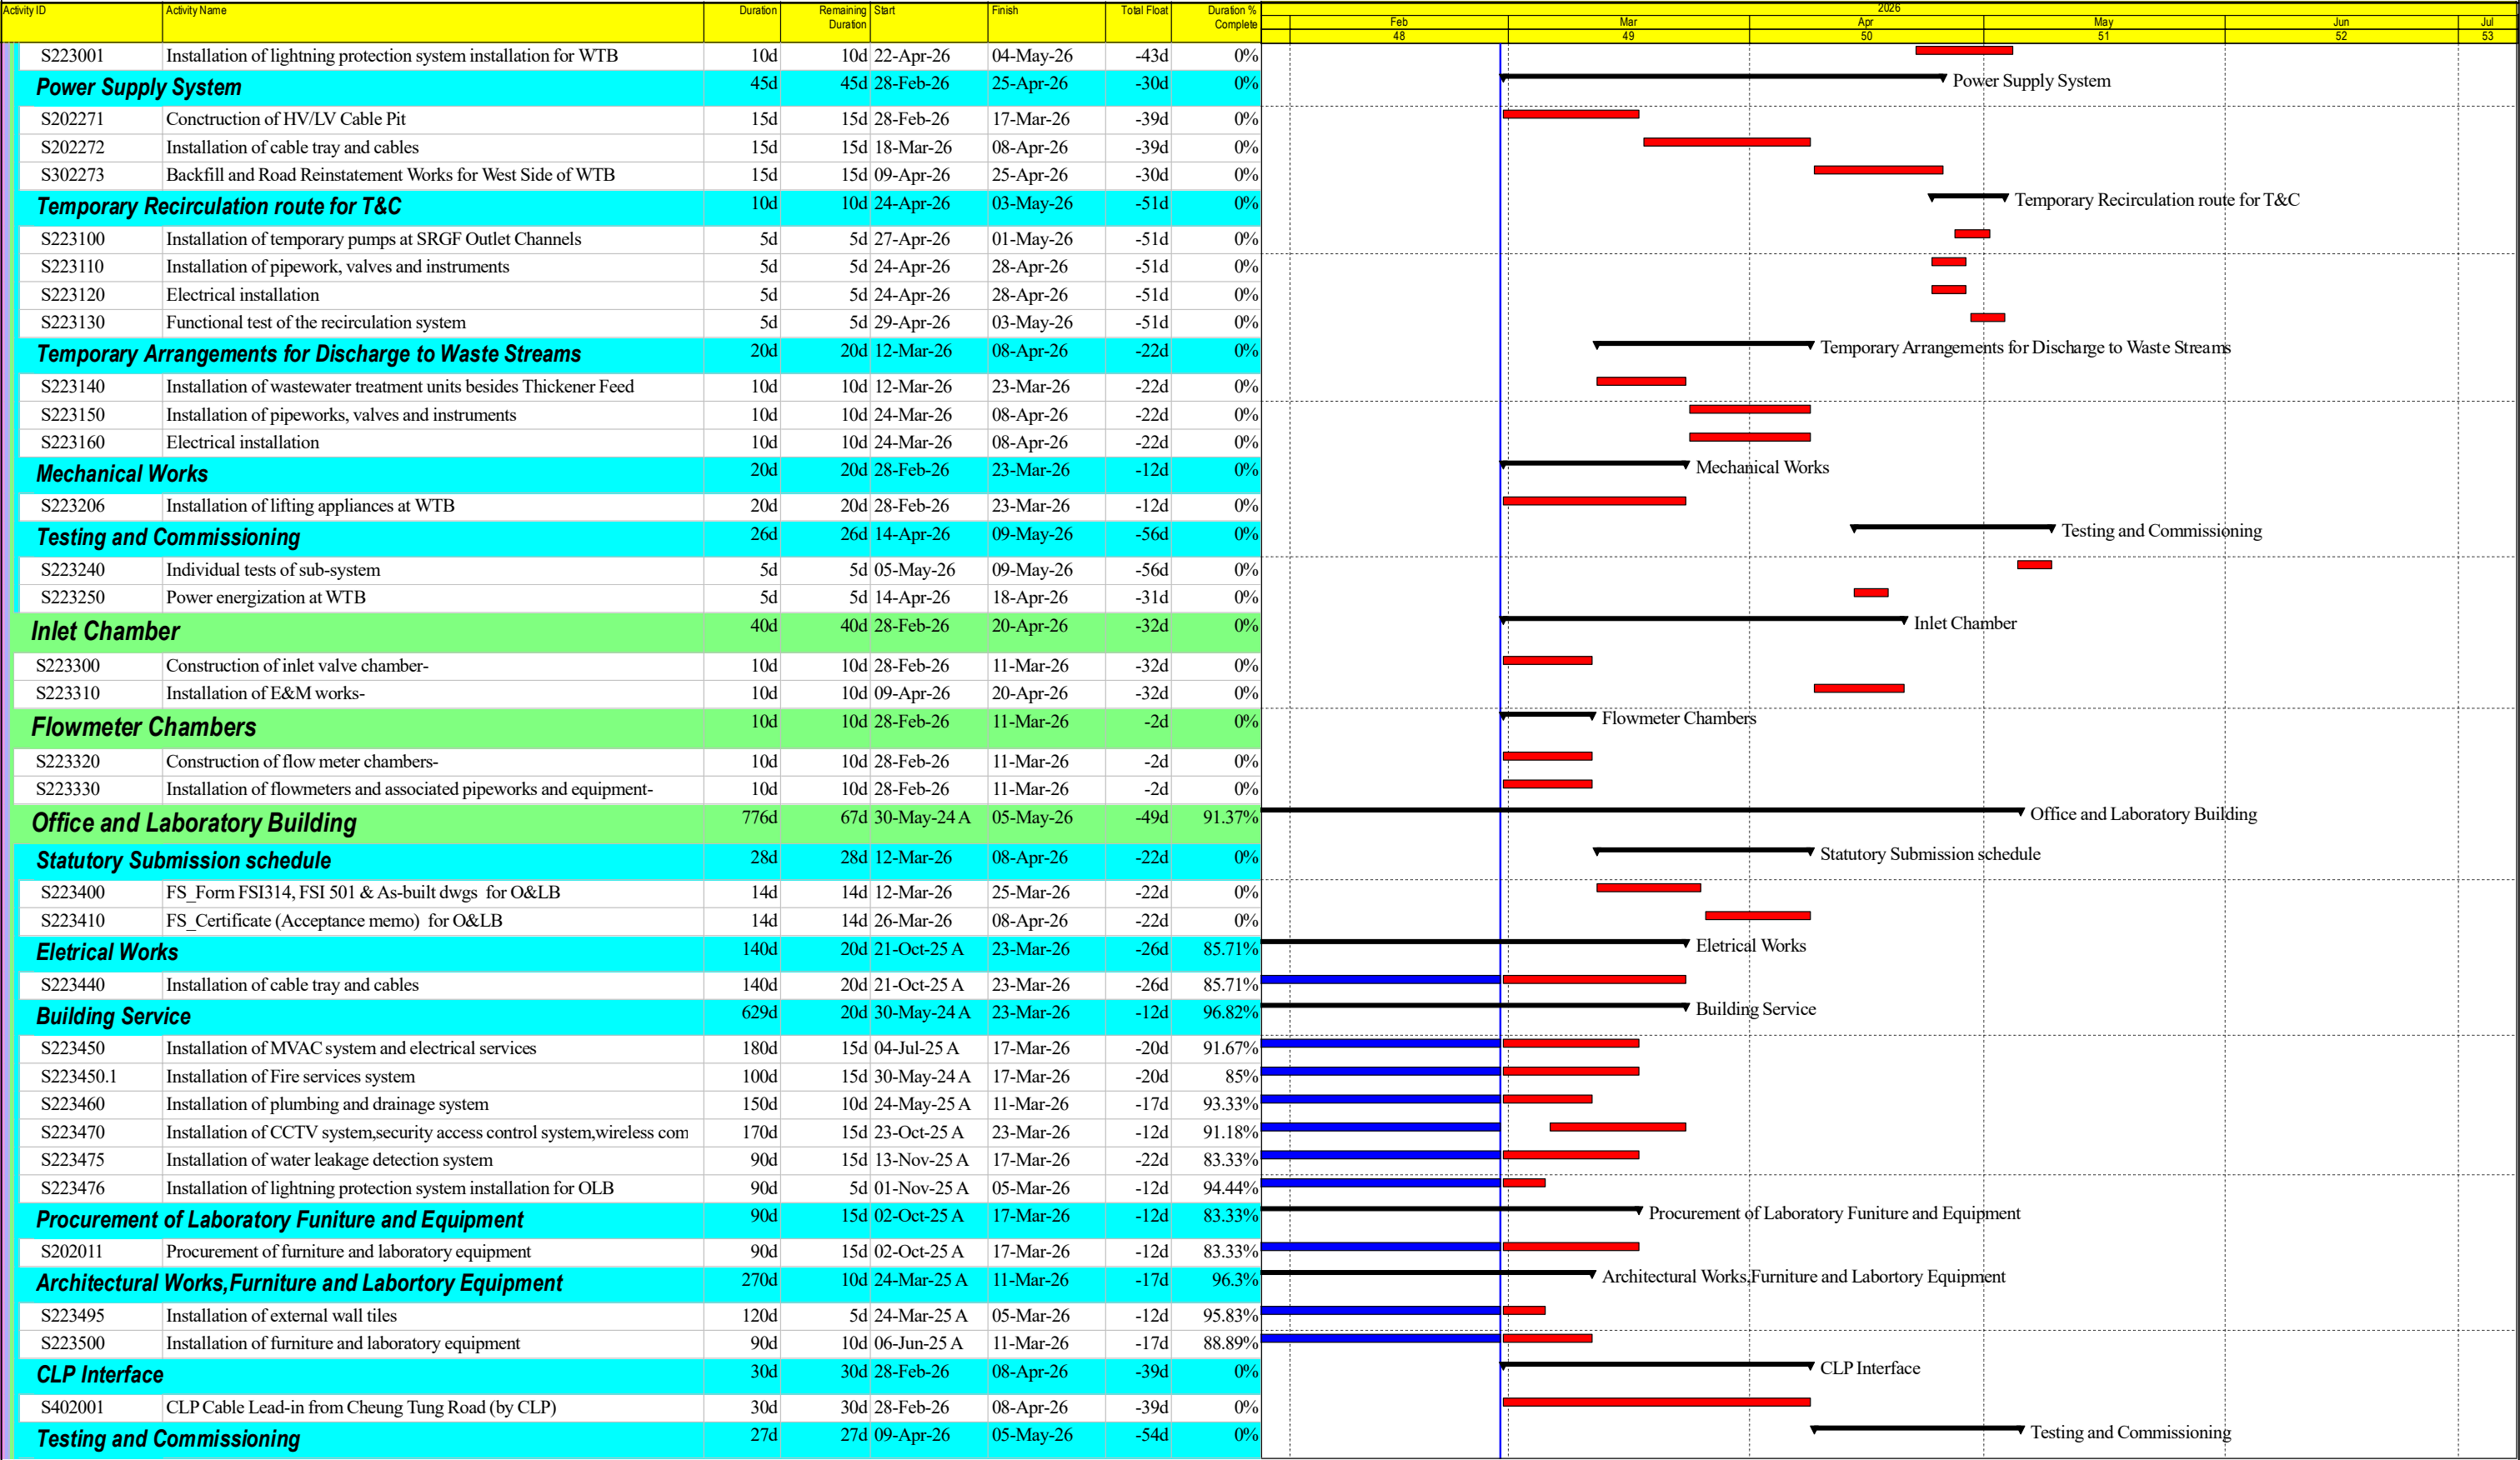

Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

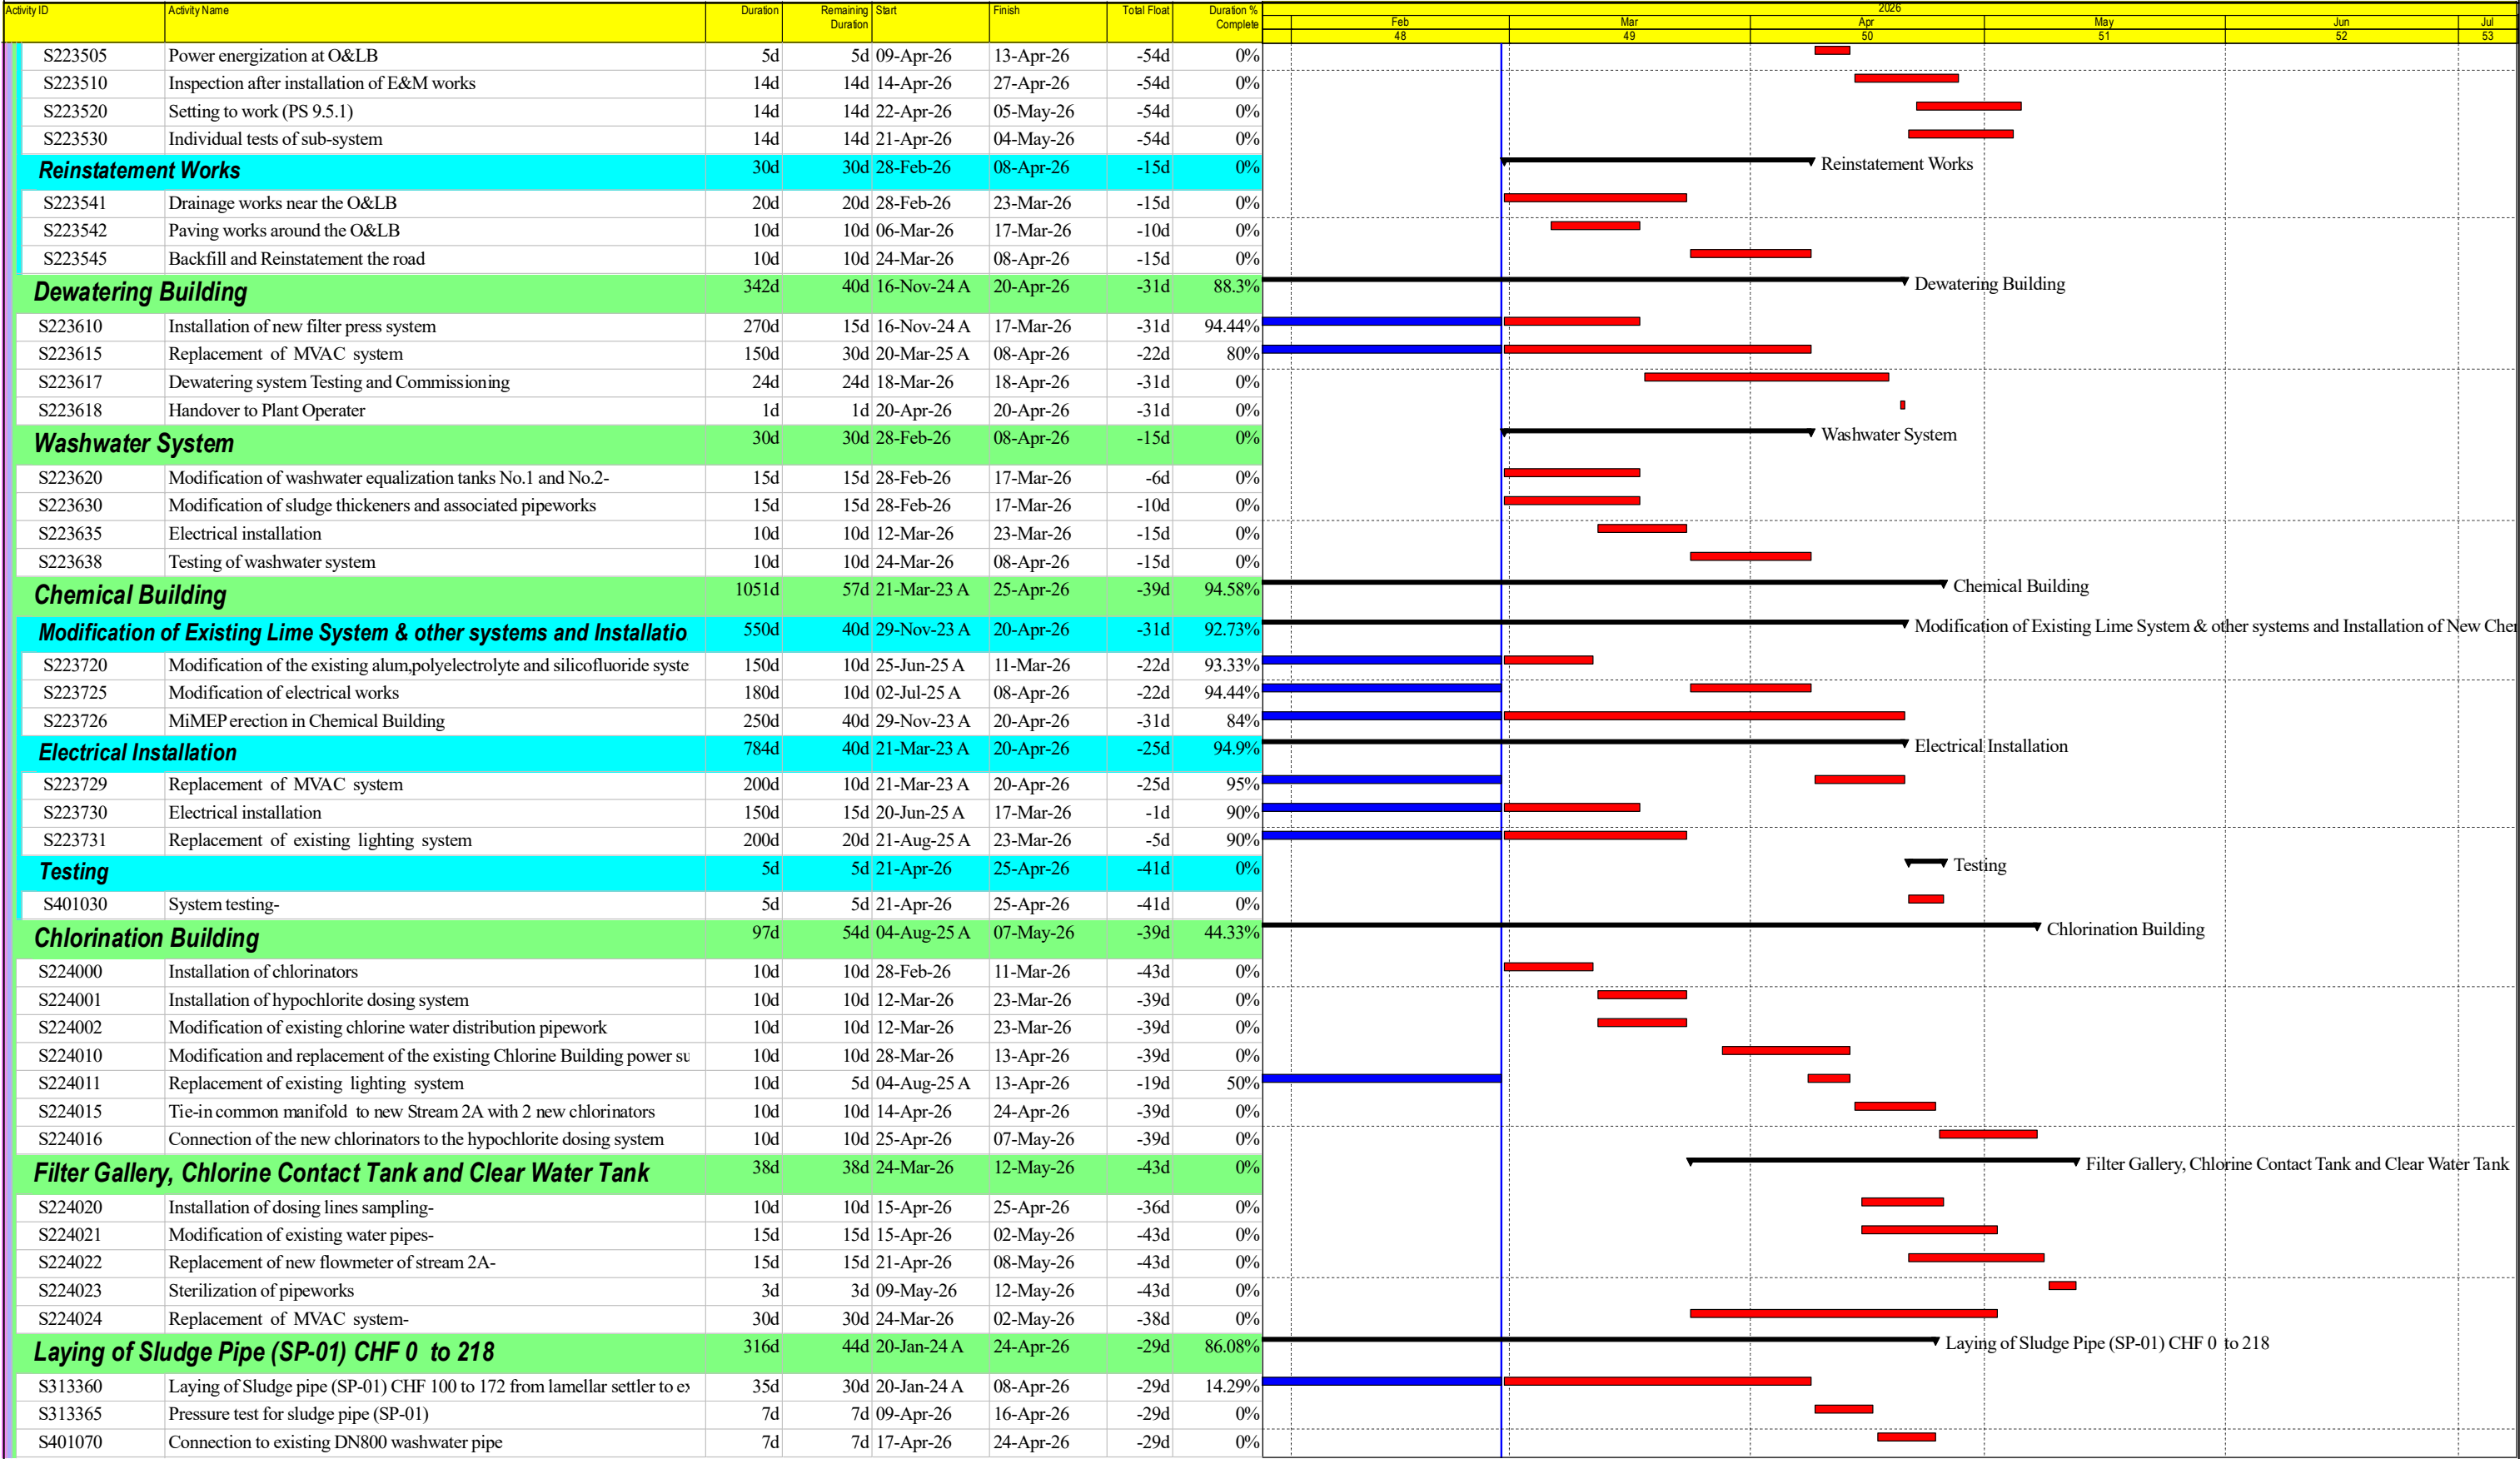


Date	Revision	Checked	Approved
28-Feb-26	1	CLX	RM

3 Month Rolling Programme -
Mar 2026 to May 2026

Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

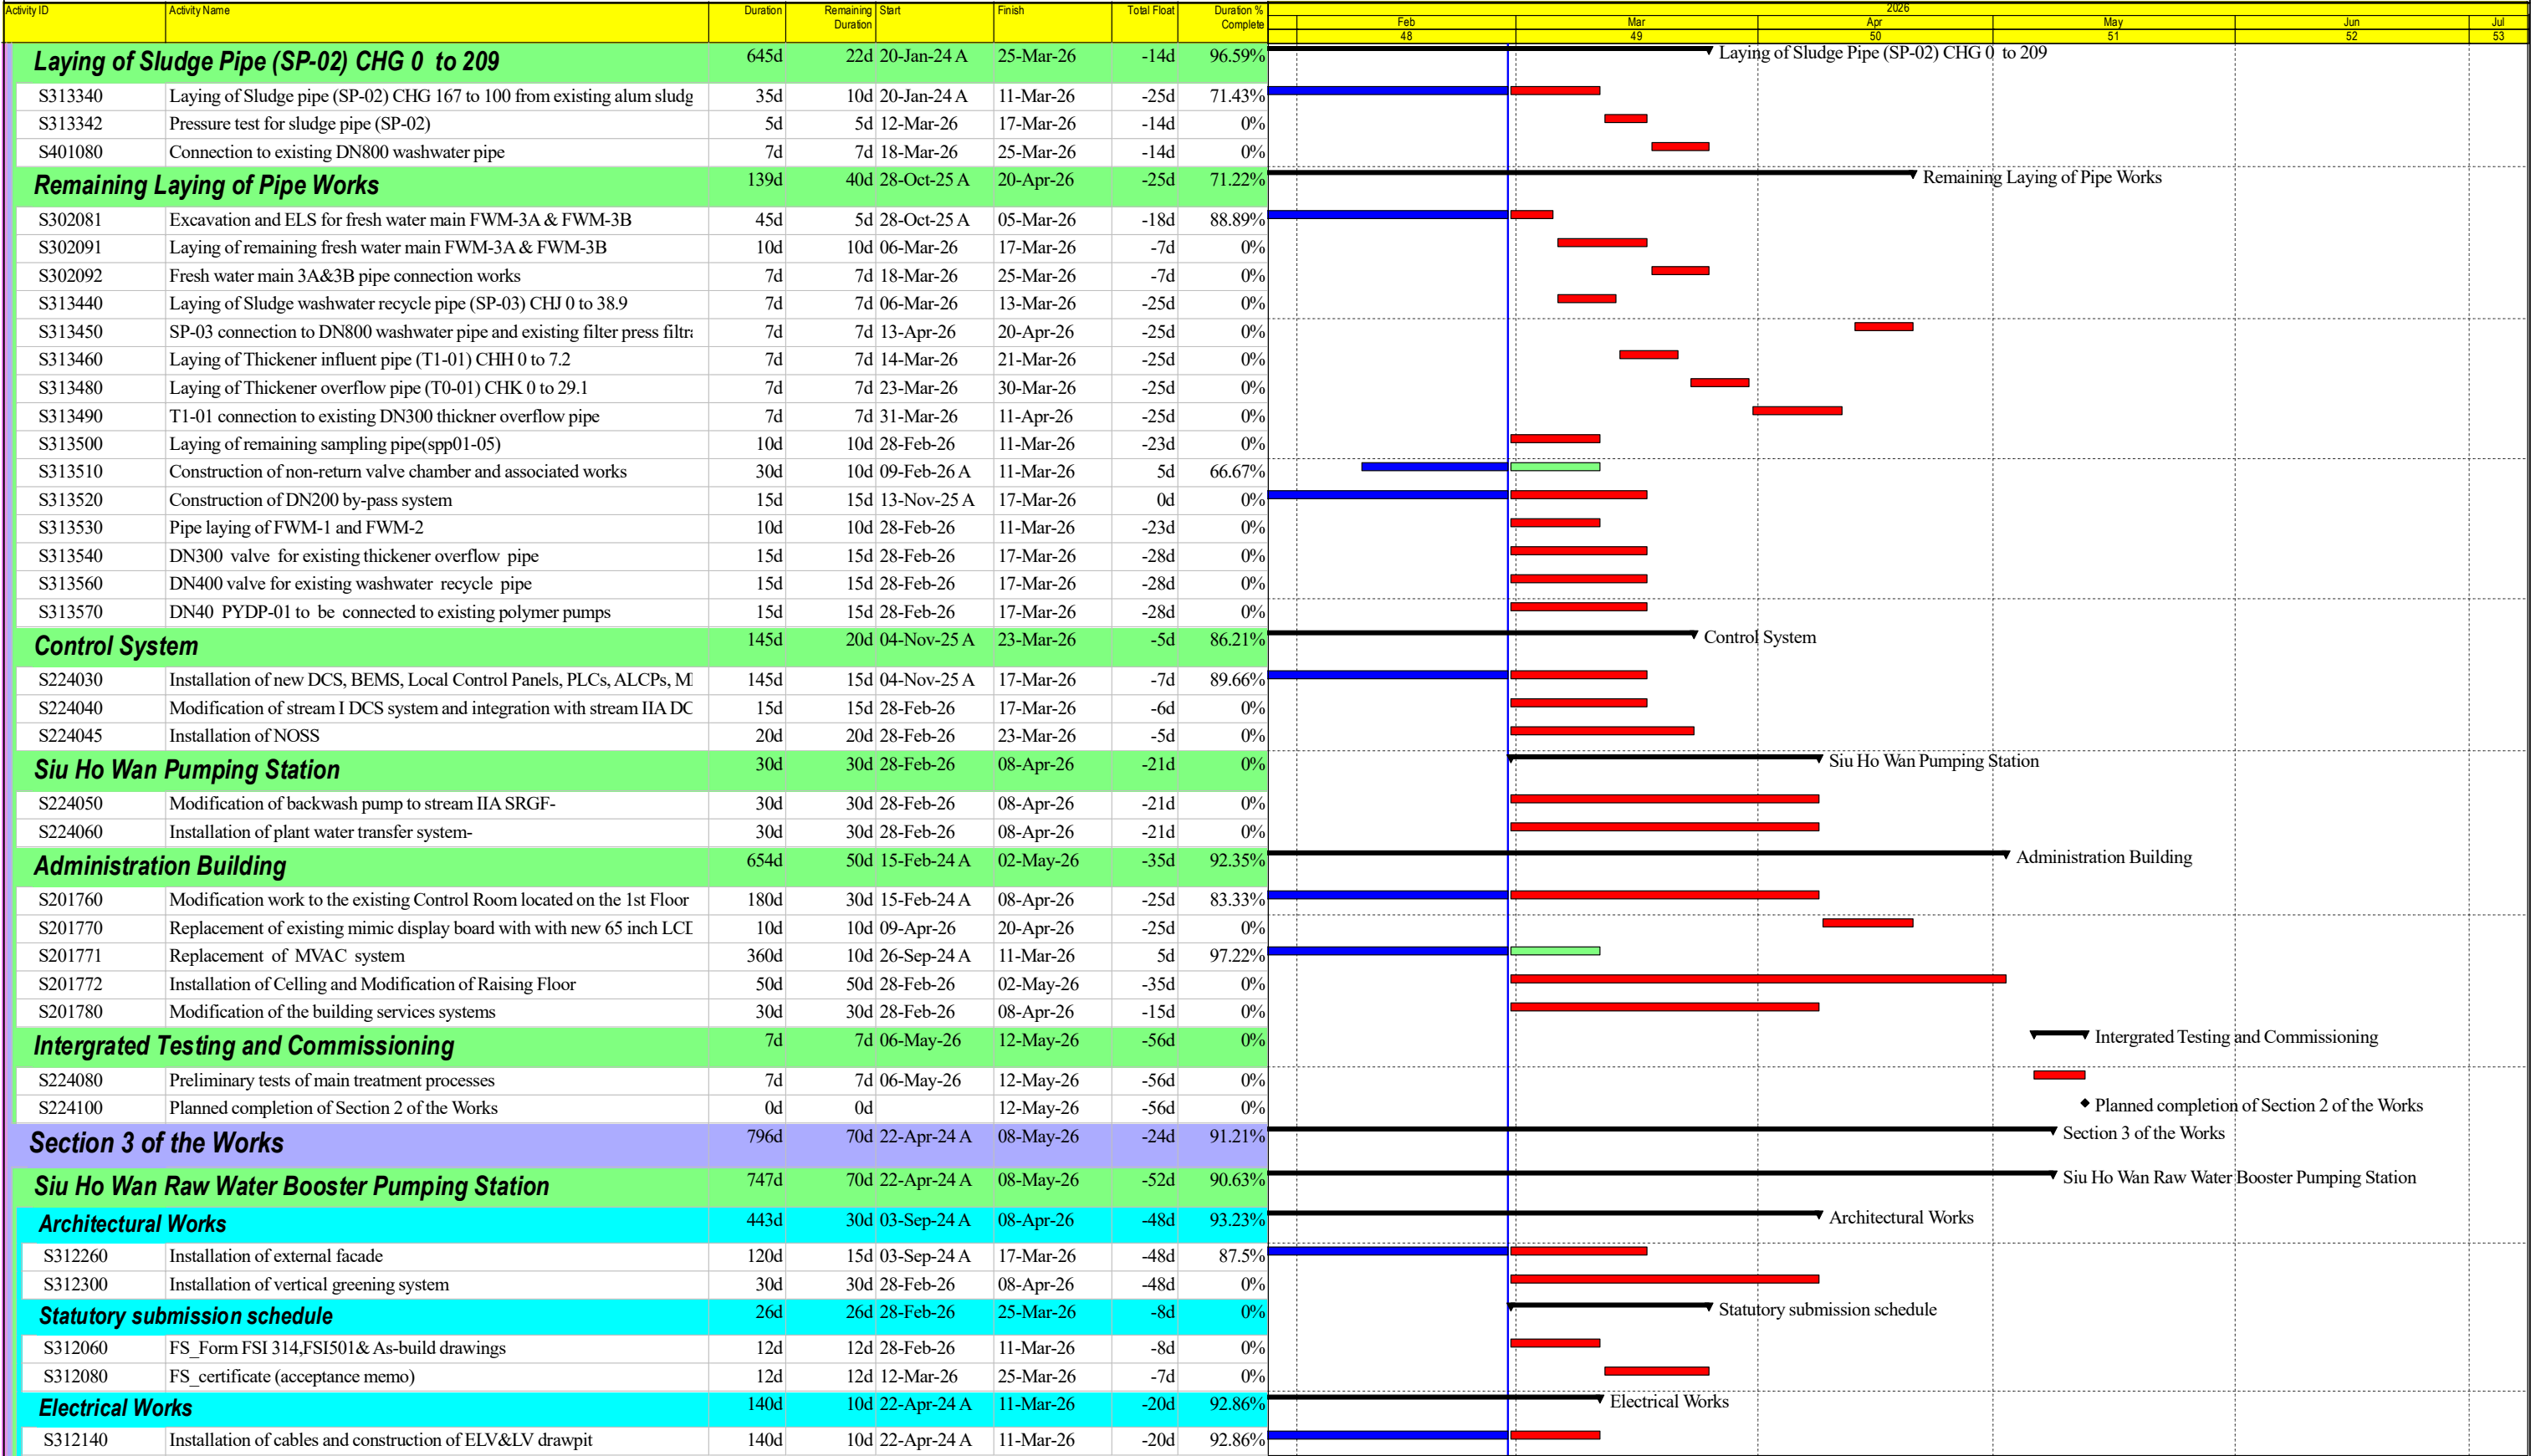

Actual Work
Non-Critical Activity
Critical Activity
◆ Milestone

Summary


Date	Revision	Checked	Approved
28-Feb-26	1	CLX	RM

3 Month Rolling Programme -
Mar 2026 to May 2026

(sheet 8 of 10)

Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

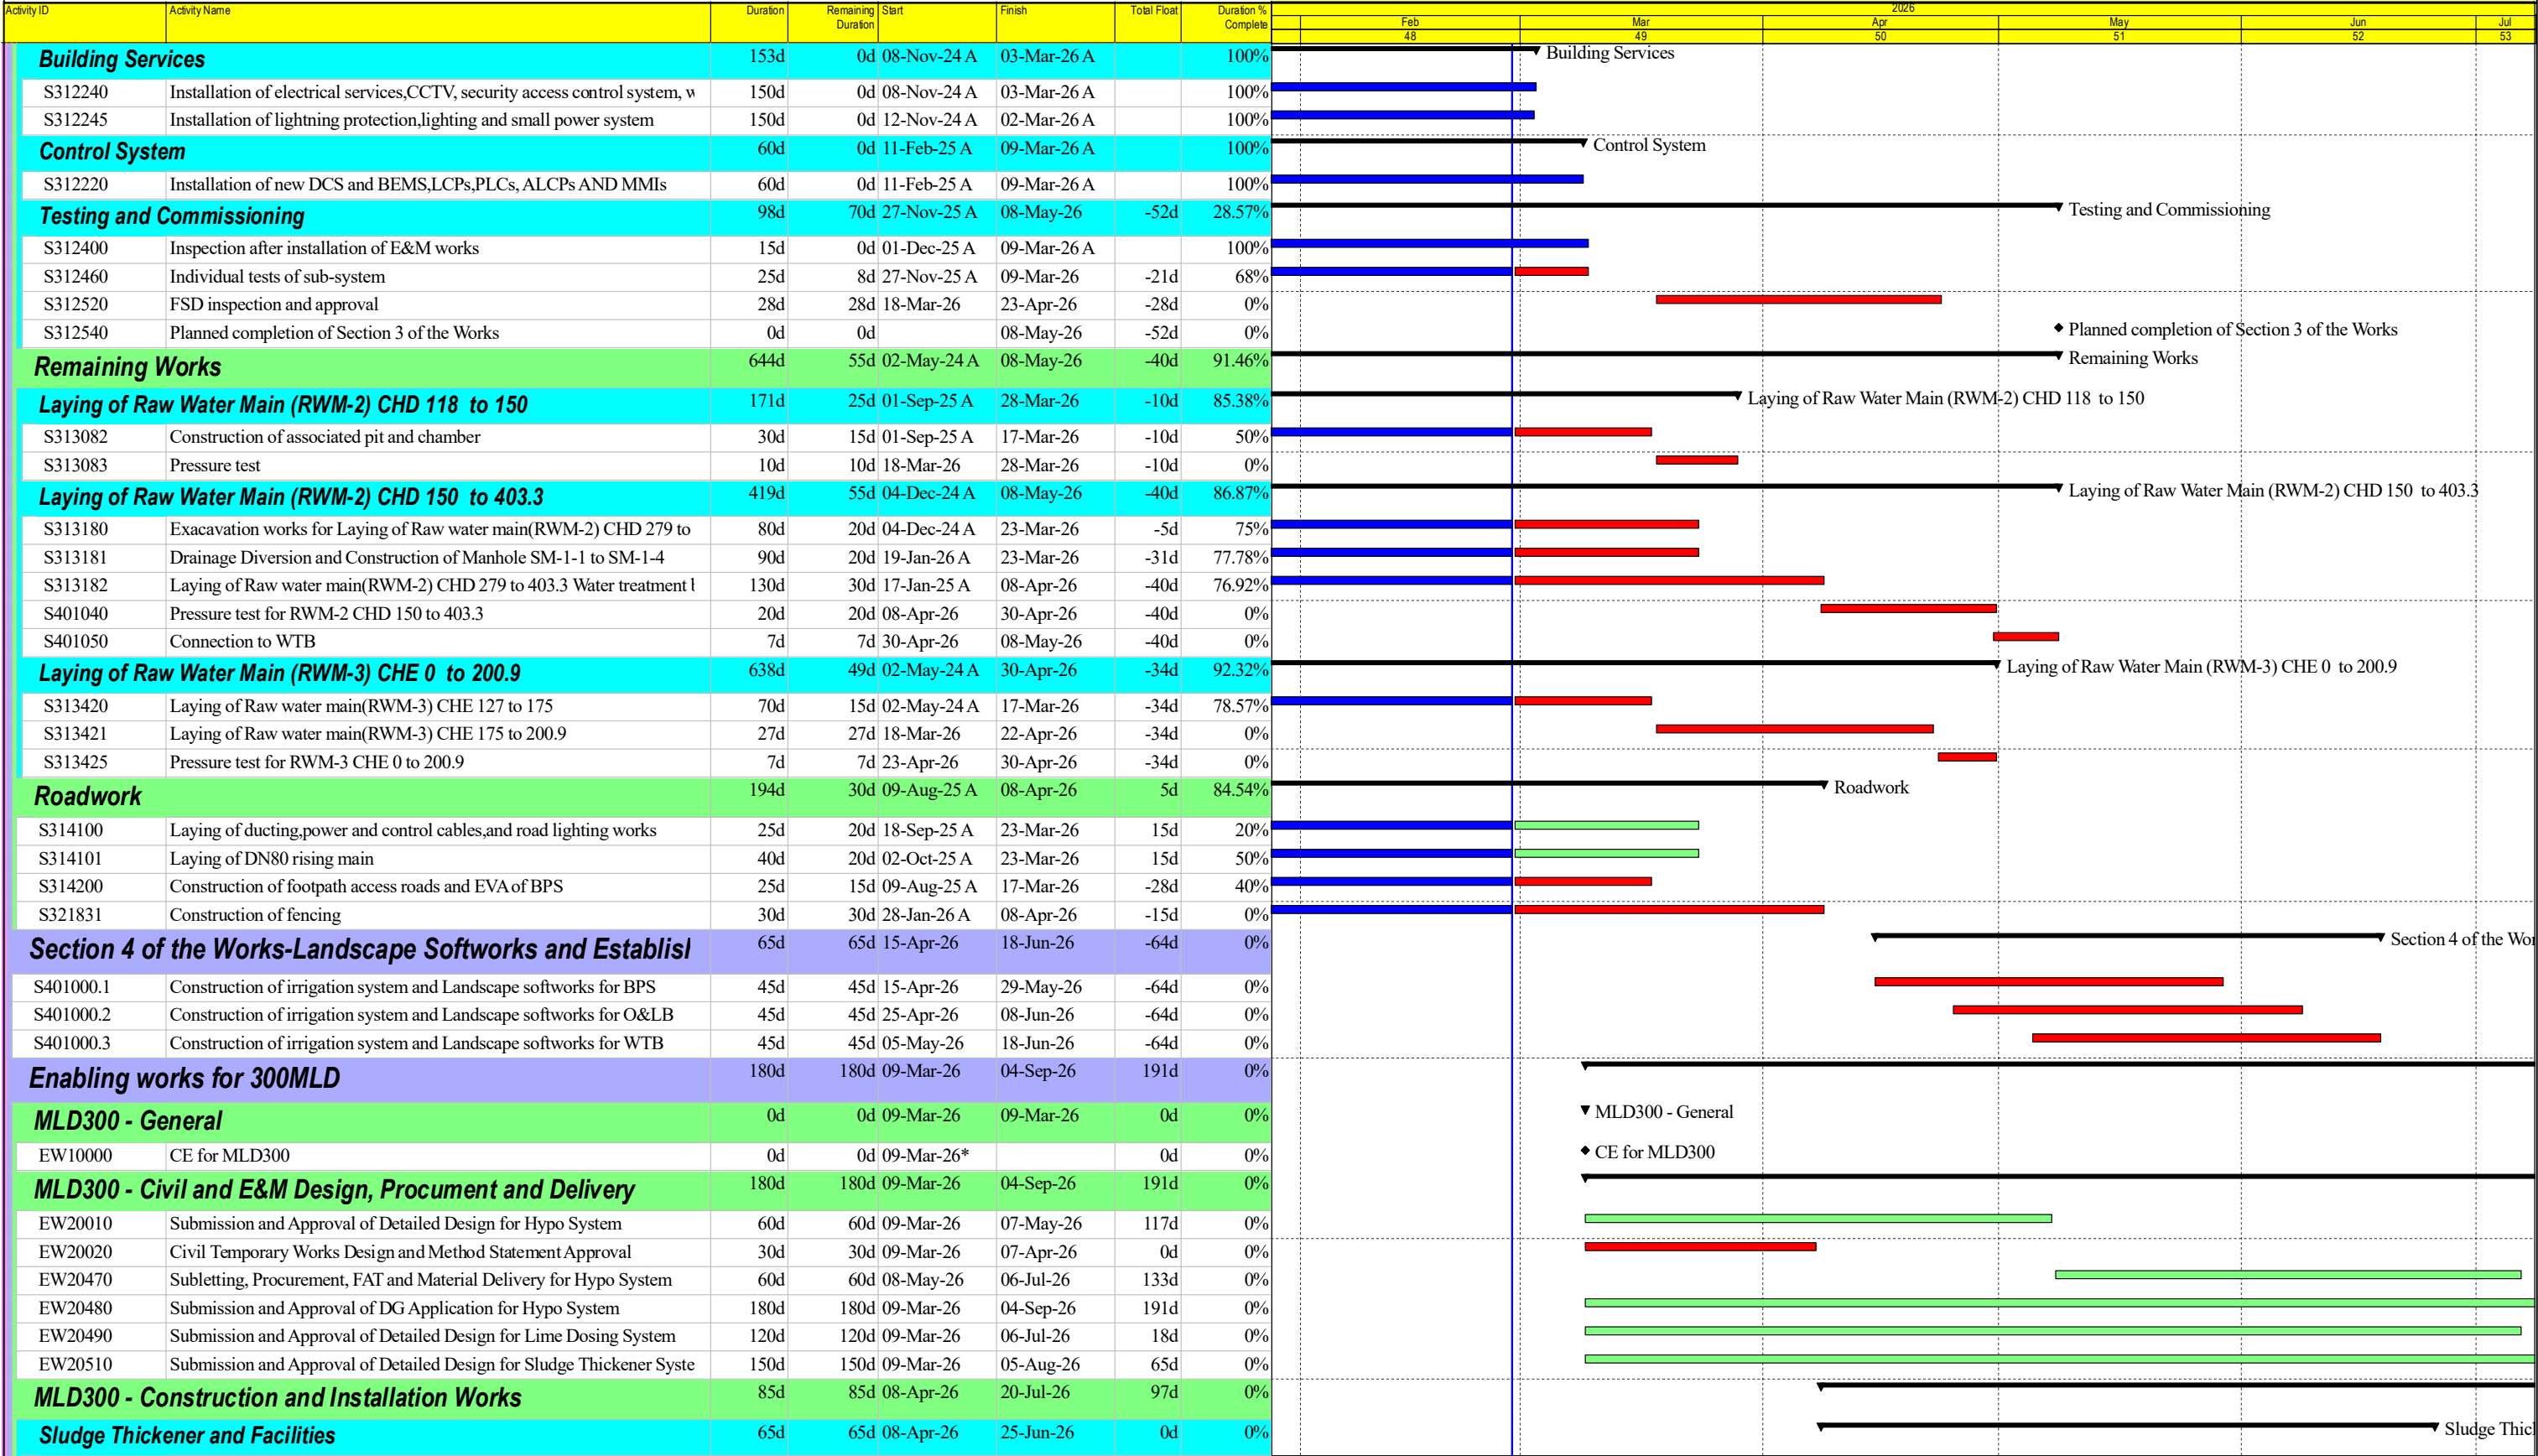

Actual Work
Non-Critical Activity
Critical Activity
Milestone

Summary

Date	Revision	Checked	Approved
28-Feb-26	1	CLX	RM

3 Month Rolling Programme -
Mar 2026 to May 2026

(sheet 9 of 10)

Contract No. 7/WSD/21 Construction of Siu Ho Wan Water Treatment Works Extension and Siu Ho Wan Raw Water Booster Pumping

Data Date:28-Feb-26

Activity ID	Activity Name	Duration	Remaining Duration	Start	Finish	Total Float	Duration % Complete	2026											
								Feb		Mar		Apr		May		Jun		Jul	
								48		49		50		51		52		53	
EW20030	Run-in construction for access	14d	14d	08-Apr-26	23-Apr-26	0d	0%												
EW20040	Site clearance, temporary drainage system and trial pit for site area	21d	21d	24-Apr-26	19-May-26	0d	0%												
EW20060	Open cut to formation level (+27.9mPD) and Pouring blinding layer	30d	30d	20-May-26	25-Jun-26	0d	0%												
External works		60d	60d	08-May-26	20-Jul-26	97d	0%												
EW20450	DN50 pipes laying from hypo system to filter gallery	60d	60d	08-May-26	20-Jul-26	97d	0%												



中國路橋
CRBC

- Actual Work
- Non-Critical Activity
- Critical Activity
- Milestone

Summary

Date	Revision	Checked	Approved
28-Feb-26	1	CLX	RM

3 Month Rolling Programme -
Mar 2026 to May 2026

(sheet 10 of 10)
